ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	ID
0		**Software Development**	**46 days**	**Tue 16/01/18**	**Tue 20/03/18**			**0**
1		**Overall**	**46 days**	**Tue 16/01/18**	**Tue 20/03/18**			**1**
2		**Design Prototype**	**6 days**	**Tue 16/01/18**	**Tue 23/01/18**			**2**
3		Create Diagrams	2 days	Tue 16/01/18	Wed 17/01/18			3
4		Create Flowcharts	2 days	Tue 16/01/18	Wed 17/01/18	3SS		4
5		Create Prototype	4 days	Thu 18/01/18	Tue 23/01/18	4		5
6		**Development**	**28 days**	**Wed 24/01/18**	**Fri 02/03/18**	**2**		**6**
7		Set up Firebase	6 days	Wed 24/01/18	Wed 31/01/18			7
8		Connect Firebase with App	6 days	Wed 24/01/18	Wed 31/01/18	7SS		8
9		User Account Setup	6 days	Thu 01/02/18	Thu 08/02/18	8		9
10		Location Setup	6 days	Mon 05/02/18	Mon 12/02/18	9SS+2 days		10

08 11 1

Design

Project: Software Development
Date: Mon 22/01/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	ID
11		Implement Core Functionality	16 days	Fri 09/02/18	Fri 02/03/18	9		11
12		**Testing**	**6 days**	**Mon 05/03/18**	**Mon 12/03/18**	**6**		**12**
13		Whitebox Testing	6 days	Mon 05/03/18	Mon 12/03/18			13
14		Blackbox Testing	6 days	Mon 05/03/18	Mon 12/03/18	13SS		14
15		Presentation	6 days	Tue 13/03/18	Tue 20/03/18	12		15

08 11 1

Project: Software Development
Date: Mon 22/01/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

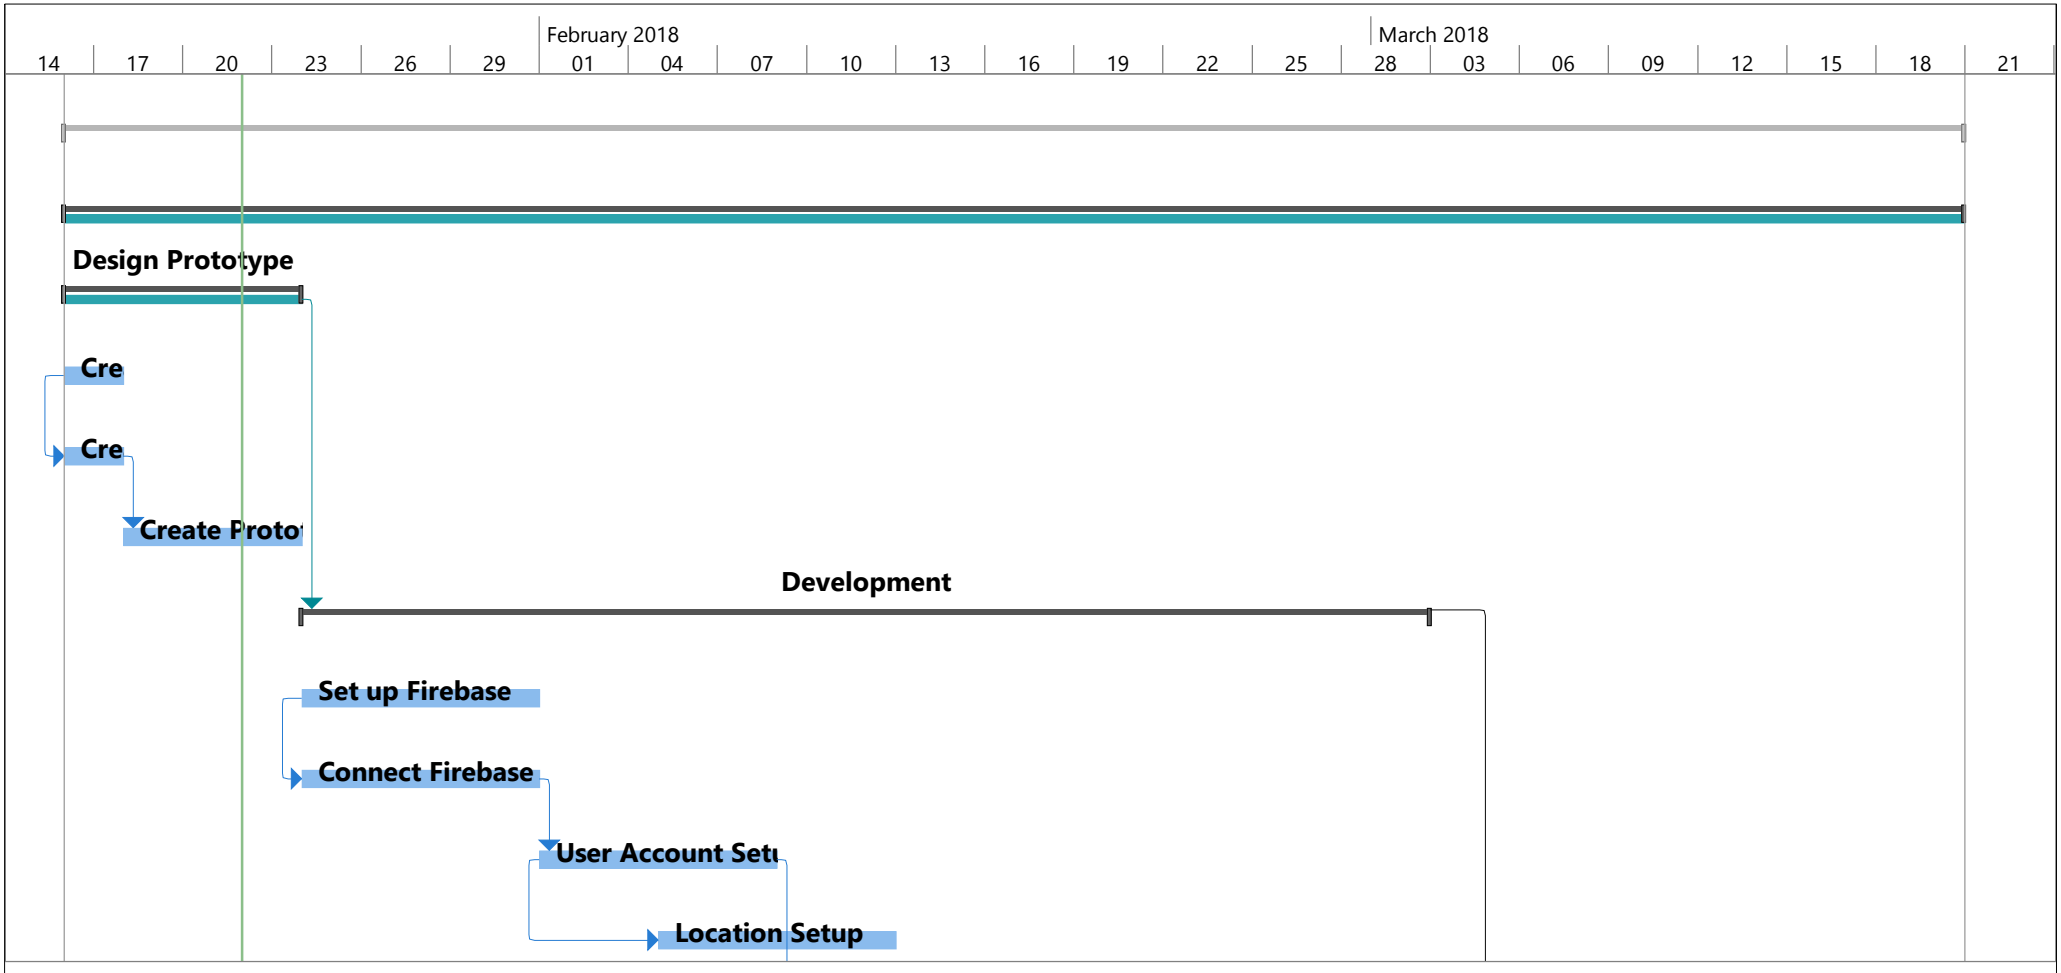

Project: Software Development
Date: Mon 22/01/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

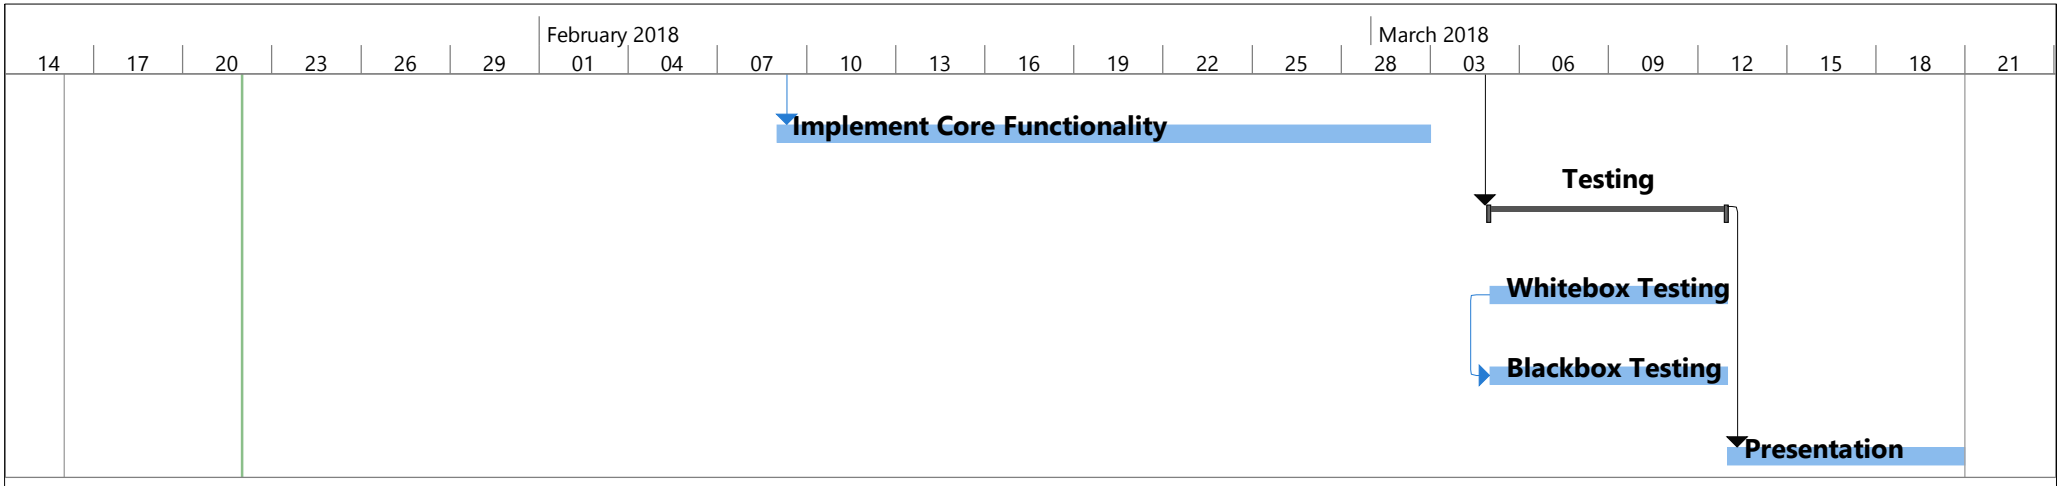

Project: Software Development
Date: Mon 22/01/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
